COMMUNITY SERVICES COMMITTEE REPORT

Group: Community Services Month/Year of Report: September 2015

Executive Director:

Ron Qualls

Phone: E-mail:

I. Budget Highlights

- 1. Tribal Individual Water/Sewer Funds 87% expended. Additional \$300k in water/sewer funding received last month has been committed in contracts for services.
- 2. Tribal Community Water/Sewer Funds 97% expended

II. Program Highlights

a.) Balanced Scorecard Measures

- 1. Trained 138 food handlers
- 2. Repaired sewer and/or water facilities for 21 homes
- 3. Installed sewer and/or water facilities for 25 homes

b.) Accomplishments


- 1. Gore WTP approximately 90% complete.
- 2. Hwy 82C Waterline project progressing. Approximately 34,600 LF (80%) complete.
- 3. Locust Grove water loss study about 95% complete
- 4. Cherry Tree Lift Station bids opened. Contract Awarded to Bronze Oak Construction. Contractor preparing submittals.
- 5. Preparing to bid Marble City Lift Station project.


c.) Future Plans

- 1. Preparing to bid out for contracts to install aerobic systems and water wells in FY 2016.
- 2. Preparing spending plan to help ensure FY16 funds will last 12 months. This might result in delays in some services but will be necessary to keep from running out of funds before the end of the FY.

Reh	Rehab/Emergency/Handicap Accessibility/LBP	Handicap Access	ibility/LBP	
Month/Yea	Month/Year of Report: October 01, 2014 Thru September 29, 2015	er 01, 2014 Thru Se	ptember 29, 2015	
	Incomplete	Completed		Total Jobs
	Application	Applications	Completed Jobs this	Completed FY
County	Submitted	Submitted	Month	2014
Adair	22	30	121	133
Cherokee	10	25	4 1	148
Craig	0	0	0	8
Delaware	9	13	1	69
Mayes	7	10	L	56
McIntosh	0	0	0	0
Muskogee	6	7	2	31
Nowata	-	0	0	9
Ottawa	0	-	-	6
Rogers	6	14	2	14
Sequoyah	2	18	8	130
Tulsa	8	12	2	10
Wagoner	-	_	0	2
Washington	~	T	0	8
Total	62	129	46	627


Force Account has 23 open work orders and is working on 4 jobs. We currently have 70 jobs posted on the web site of which 23 have been rebid in the last 3 weeks due to no bids.

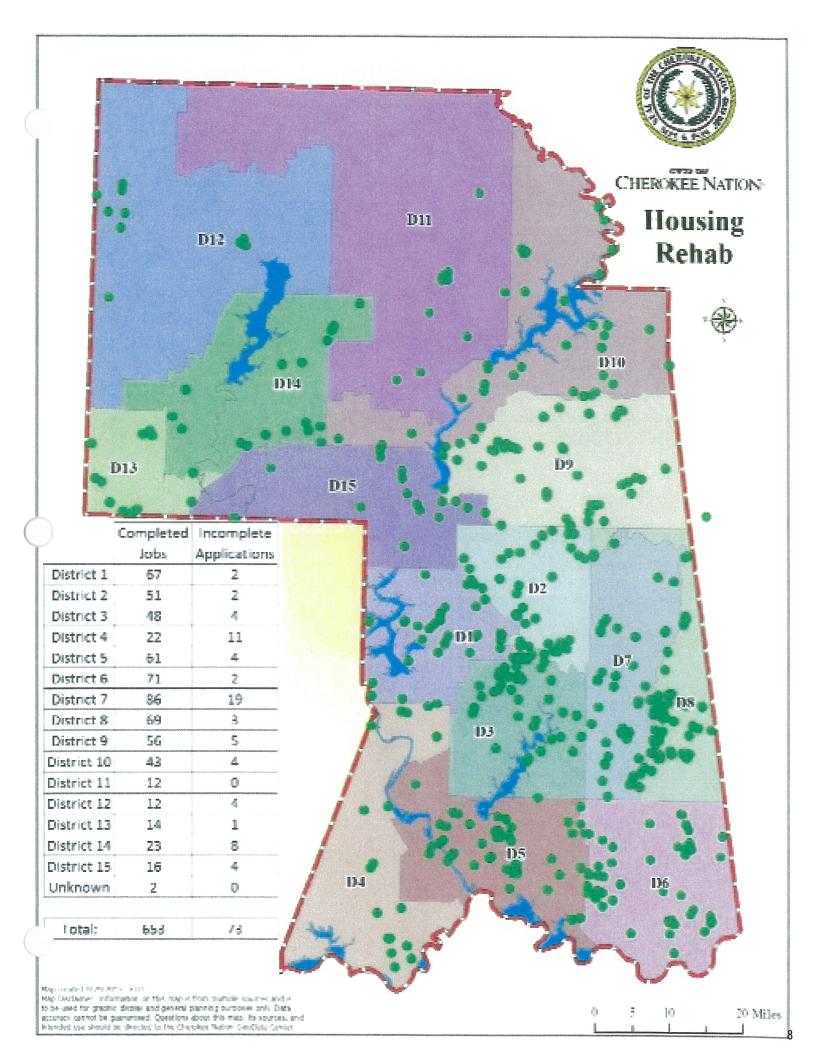


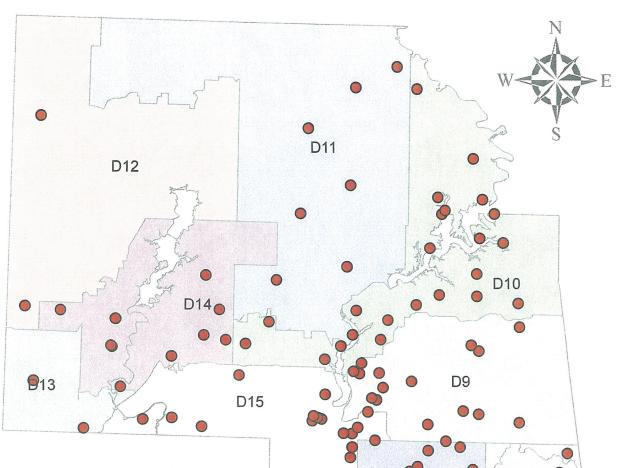

Water & Sanitation Open Applications September 2015

Council District	# of homes
D1	12
D2	12
D3	26
D4	9
D5	10
D6	14
D7	8
D8	7
D9	16
D10	22
D11	8
D12	2
D13	2
D14	11
D15	16

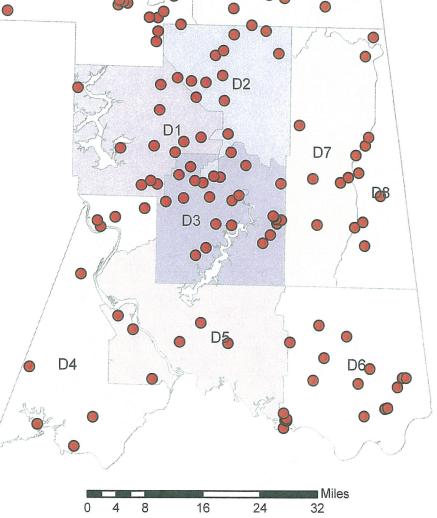

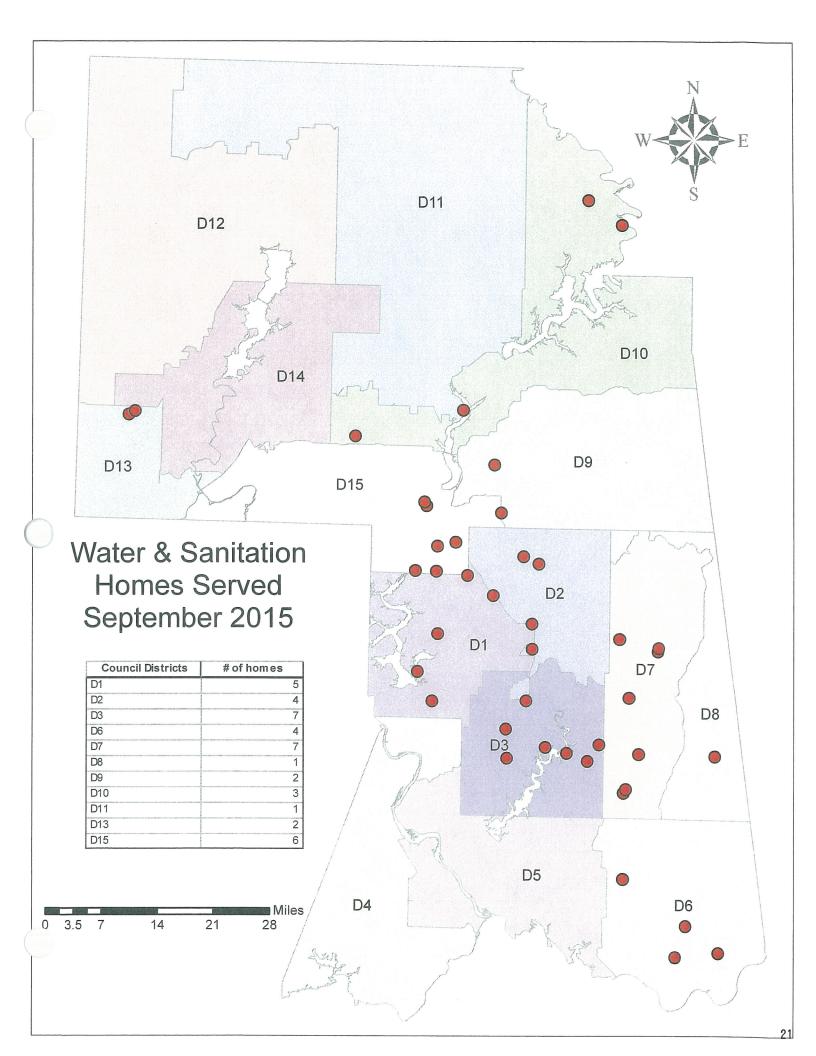

CHEROKEE NATION TRIBAL COUNCIL COMMUNITY SERVICES COMMITTEE REPORT

Group:	Housing Authority	_	Month/Year of Report:	Octob	er, 2015	
Executive Director Deputy Director	· ·	_	Phone:	918-4	56-5482	
MAP Foreclosu	re Report	Foreclosure	Date			
Case		Notice	Assistance	Type of	Amount Due	
Number	County	Received	Received	Assistance	HACN	

None to report

Reflects only those where HACN is the mortgage holder (pre-May'08)

Public Disclosures:

As required by 24 CFR Part 1000.30, services provided to Cherokee Nation Housing Services Employees and Employee relatives from funds received pursuant to the Native American Housing Assistance and Self-Determination Act of 1996 (NAHASDA), shall be publicly disclosed.

The following applicants have been determined eligible for participation.

LOW RENT APARTMENT:

The following employee and/or relatives were approved to receive services for Low Rent Apartment pursuant to guidelines set forth in the Housing Policy as approved by the Principal Chief of the Cherokee Nation and HACN Policy as approved by the Board of Commissioners.

None to report

HOMEOWNERSHIP:

The following employee and/or relatives were approved to receive services for Homeownership program pursuant to guidelines set forth in the Housing Policy as approved by the Principal Chief of the Cherokee Nation and HACN Policy as approved by the Board of Commissioners.

None to report

RENTAL ASSISTANCE/TEMPORARY RENTAL ASSISTANCE/COLLEGE HOUSING:

The following employee and/or relatives were approved to receive services for Rental Assistance program pursuant to guidelines set forth in the Housing Policy as approved by the Principal Chief of the Cherokee Nation and HACN Policy as approved by the Board of Commissioners.

Taya England, cousin of Gina Salazar an employee of HACN Wanda Duncan, cousin of Dora Watie an employee of HACN Patricia Davis, sister of George Hubbard of CN-Housing Rehab Patricia Davis, sister in law of Shirley Hubbard of HACN Cody Henson, aunt is Sally Cummins of HACN Johnny Johnson, brother in law is Jarrod Proctor of CN-Hsg Rehab Victoria Hoskin, cousin is Charles Hoskin, Jr, CN - Sec of State Victoria Hoskin, uncle is Charles Hoskin an employee of CN Ashley Cheater, father is Terry Cheater an employee of HACN Dennis Ely, mother is Rebecca Ely of CN-Community Services Tanner Ely, mother is Rebecca Ely of CN-Community Services Deonna Toney, mother is Cassie Wedge of CN-Human Services Deonna Toney, aunt is Pauline Pettit of CN-Human Services Erik Claphan, aunt is Wanda Hatfield, CN Tribal Council Casey Collyge, grandfather is Curtis Snell, CN Tribal Council Laura Latta, uncle is Jeff Adair of HACN Jana Still, an employee of CN - ICW Shawn Lochner, uncle is Ray Caviness of CN-Housing Rehab Holly Hiatt, aunt is Erna Reeves of HACN Trista Vaughn, mother is Teresa Webber of CN-ICW

NEW CONSTRUCTION HOMEOWNERSHIP PROGRAM: (Non-NAHASDA Program)

The following employee and/or relatives were approved to receive services for the New Construction Homeownership program pursuant to guidelines set forth in the HACN Policy as approved by the Board of Commissioners.

Kelby Elam, father is Joe Locust of HACN Caylan Godwin, mother is Lista Godwin of HACN



Keys to a brighter future

Announcements

Board of Commissioners Meeting:

Tuesday, October 27th at 5:30 - Regular Meeting

Office Closures:

None

All offices and staff of the HACN may be reached through the main office number, regardless of their office location. The local and toll free numbers are:

918-456-5482

800-837-2869

Housing Authority of the Cherokee Nation Month Ending: August, 2015

Current Program Participants:

			Rei	Rental Assistance	2)	Homeov	Homeownership	707	Loans	Totals	als
	Community		Rental	Temporary	College	Home-	New	Title VI	Assumable/	Total	
	Shield	Low Rent	Assistance	Assistance	Housing	ownership	Construction	Mortgage	Other Mtg.	Housing	% of
County	Insurance	Apartments	(RAP)	(TAP)	Programs	Programs	Homes	Program	Program	Participants	Participants
Adair	472	151	123	4	11	120	37	18	-	937	15%
Cherokee	546	171	322	12	24	288	81	63	9	1,513	23%
Craig	42	55	28	2	0	11	9	2	0	146	2%
Delaware	340	118	95	5	12	93	33	22	0	718	11%
McIntosh	12	N/A	0	0	0	9	2	0	0	20	%0
Mayes	234	121	71	7	12	29	22	16	0	550	%6
Muskogee	140	52	89	3	0	59	19	18	0	359	%9
Nowata	29	41	28	0	₽	10	16	2	0	127	2%
Ottawa	18	N/A	F	0	1	7	2	5	0	34	1%
Rogers	141	72	191	10	0	87	20	43	5	695	%6
Sequoyah	544	N/A	204	13	17	182	28	58	3	1,049	16%
Tulsa	09	N/A	111	8	4	24	2	3	0	212	3%
Wagoner	10	N/A	9	0	2	62	1	1	0	82	1%
Washington	30	38	41	1	0	27	9	3	0	146	2%
Total:	2,618	819	1,289	65	84	1,043	275	254	15	6,462	100%
				1 / 38		13	1 318)(696		

Current Applications:

			Community						
	Mortgage	NAHASDA	Shield	Low Rent	Rental	New Home	%	Total	% of
County	Assistance	Home-ownership	Insurance	Apartments	Assistance	Construction	NHCP	Apps	Total
Adair	0	22	12	207	164	108	%/	513	12%
Cherokee	0	21	17	235	333	407	25%	1,013	23%
Craig	0	3	0	36	19	30	2%	88	7%
Delaware	0	36	8	167	101	195	12%	507	12%
McIntosh	0	0	0	0	0	13	1%	13	%0
Maves	0	29	7	74	82	131	8%	323	7%
Muskogee	0	26	3	65	72	136	%8	302	7%
Nowata	0	1	1	39	21	32	2%	94	7%
Ottawa	0	F	0	0	12	22	1%	35	1%
Rogers	0	32	8	163	147	124	%8	474	11%
Seguoyah	0	38	16	0	193	232	14%	479	11%
Tulsa	0	27	П	0	153	121	7%	302	7%
Wagoner	0	5	0	0	12	27	2%	44	1%
Washington	0	19	1	84	53	47	3%	204	. 5%
Total:	0	260	74	1,070	1,362	1,625	100%	4,391	100%

Mortgage Assistance applications transferred to CN Commerce in April, 2014

New Construction Homeownership Program Development Files Processing

Month of: Aug, 2015

	uo	Constructi Complete	37	81	9	33	2	22	19	16	2	20	28	2	П	9	275	
		Under Constructi	19	52	1	30	0	7	13	9	3	12	46	2	2	9	205	
	tnə	Developm Developm	22	57	18	09	2	31	29	17	80	13	36	17	2	9	318	
	∄uį	ln Process	14	23	2	35	0	23	6	н	2	4	11	1	0	4	129	
	Construction	Construction Complete	37	81	9	33	2	22	19	16	2	20	28	2	1	9	275	480
	Cons	Under / Ready Const	19	52	1	30	0	7	19	9	3	12	46	2	2	9	205	
	Stg IV	Process Closing	13	36	12	33	2	21	10	9	2	9	21	2	1	1	166	
	Stg III	Survey Rec'd	0	0	2	1	0	0	0	2	0	2	2	0	0	1	10	
Processing	Stg	Survey Pending	0	5	2	5	0	5	0	0	0	3	2	1	0	7	24	8.
Proce	111	Problem Files	2	2	1	1	0	0	₽	Н	0	1	1	0	0	1	11	318
	Stg II	Site Inspect	2	5	0	2	0	5	е	Э	0	1	6	0	0	1	31	
	Stg I	Prelim Review	5	6	1	18	0	0	15	5	9	0	1	14	H	1	76	
	Applications	App Processing	13	19	2	30	0	20	6	1	2	4	11	1	0	4	116	129
	Applic	App Problem	H	4	0	5	0	Э	0	0	0	0	0	0	0	0	13	1.
		Waiting List	48	270	14	71	10	62	88	14	15	95	129	112	23	34	985	
		County	Adair	Cherokee	Craig	Delaware	McIntosh	Mayes	Muskogee	Nowata	Ottawa	Rogers	Sequoyah	Tulsa	Wagoner	Washington	Total:	

STAGE I:

Copies of Deed(s), etc. Check Floodmaps/Floodplain Identify Utility Companies Contact for Site Inspection

STAGE 111:

Order/Receive Survey
Order/Receive Perc Test
Receive Utility Assurance
Receive Abstract from participant


Identify/Propose Site Plan Identify/Propose Utilities Identify/Propose Lateral Field Identify/Propose Easement(s) Deliver Utility Assurance Letters Request Abstract from participant

STAGE IV:

Survey Review / Identify Barriers / Process for Closing


New Construction Homeownership Program Application Data

							0.000								**************************************	201
/O Total	d Apps	104	358	30	% 190	13	129	% 136	% 31	% 23	% 123	% 234	% 121	% 21	47	1 500
0/M %	Land	54%	62%	%09	20%	77%	52%	%89	48%	70%	81%	73%	93%	81%	79%	/033
% With	Land	46%	38%	40%	20%	23%	48%	32%	52%	30%	19%	27%	7%	19%	21%	701/0
Without	Land	99	223	18	92	10	L 9	92	15	16	100	170	112	17	37	000 1
Has	Land	48	135	12	95	3	62	44	16	7	23	64	6	4	10	רניי
	County	Adair	Cherokee	Craig	Delaware	McIntosh	Mayes	Muskogee	Nowata	Ottawa	Rogers	Sequoyah	Tulsa	Wagoner	Washington	Total

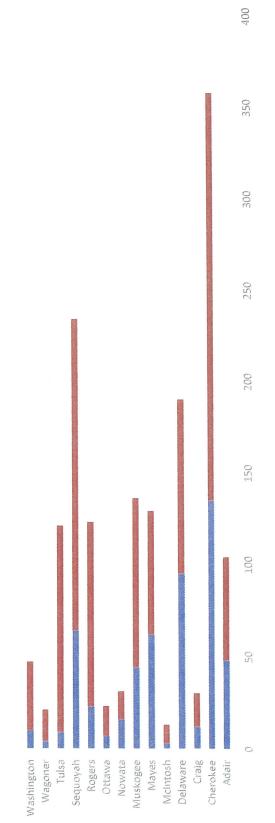

Statistics as of: August 31, 2015

HACN New Construction Program

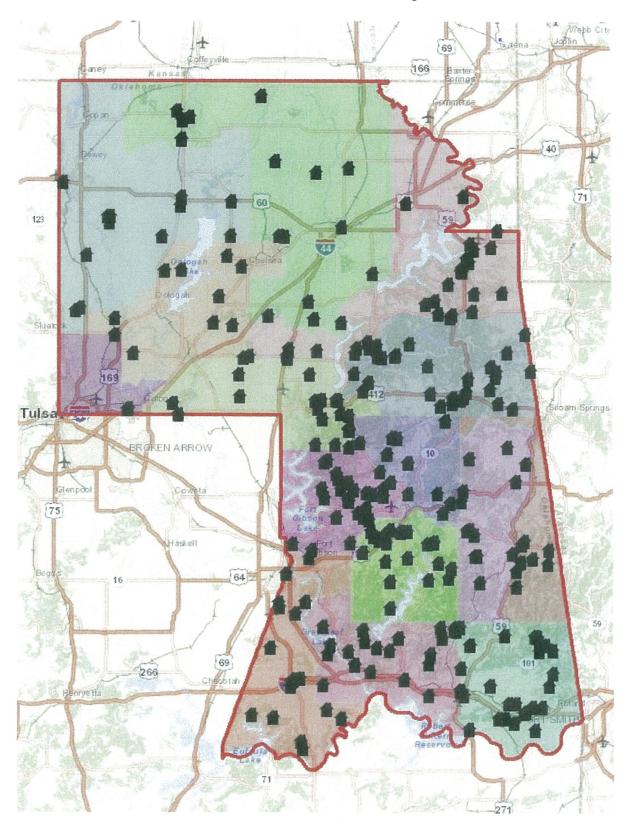

The above map is a representation of locations that the HACN has inspected sites for and/or built new homes on the New Home Construction Program.

COMMUNITY SERVICES COMMITTEE REPORT

Group: Community Services/Road and Transit Dept. Month/Year of Report: Oct 2015

Group Leader: Ron Qualls Phone: 918-453-5248 E-mail: ron-qualls@cherokee.org

I. Budget Highlights:

a.

b.

II. Program Highlights

- a) Accomplishments:
- b) Future Plans/New Initiatives
- c) Status on Other Projects:

ADAIR COUNTY PROJECTS:

- 1. Chewey Road Designer: Red Plains Engineering. RP working on 90% completion. R/W will submit for appraisals as needed.
- 2. Dahlonegah South Designer: Holloway Updike & Bellen HUB. 90% checked plans were returned for revisions on 5/14/14. Roads R/W supplied Adair County commissioner with a Notice of Interest letter to be mailed to the residents along the road.
- 3. Bell North Designer: Red Plains Engineering. RP working on 90% plans. R/W received easements and exhibits 8/27/15 and is currently performing the first check of the documents.
- 4. CNI Industrial Access Designer: D. Moore Contractor: Glover & Associates. Contract amount \$1,633,194.81.Construction underway working on subgrade and pipe placement aggregate base being placed on west end. Asphalt placed on BOP west end to sta. 30+00 30% complete
- 5. Dahlonegah West-Designer: Holloway Updike & Bellen. R/W is complete with research of ownership. Awaiting 30% set of plans.
- 6. Lyon Switch Designer: J. Shehi. HUB Engineering submitted 30% review on 11/19/14. HUB Engineering is about 75% complete with hydrology
- 7. Malloy Hollow– Designer: D. Moore. HUB Engineering Submitted Final Plans 6/15/2015. Holloway has completed their review and has signed Title Sheet.
- 8. North Salem (Bethel Road) Designer: Red Plains. RP are working on 90% Plans.
- 9. Smith Hollow Designer: Red Plains Engineering. RP are working on 90% Plans. R/W will submit for appraisals as needed.

COMMUNITY SERVICES COMMITTEE REPORT

- 10. Bell School South Designer: A. Harris Sent task order to Guy Engineering on 8/12/14 for pavement design, hydraulic study, check, and sign off on project.
- 11. Rocky Mountain School Loop- Designer: D. Moore Sent task order to Guy Engineering on 8/11/14 for pavement design, hydraulic study, check, and sign off on project.
- 12. Honey Hill Phase I Designer: HUB Engineering Design plans are complete. Next condemnation court docket is set for 10:00 AM October 5, 2015 at the Adair County Courthouse. Utility letters were sent out for estimates for relocation.
- 13. Bunch Road Designer: Nickle & Associates R/W has completed ownership research and sent it to Nickle & Associates 7/11/14. Decision was made to only do the portion from the BOP and stopping before the first railroad crossing. New task order was issued on 9-18-14 for the revised length of project.
- 14. Oak Ridge Road and Oak Ridge Extension Designer: CGA Engineering. R/W has completed ownership research for Oak Ridge and mailed it 2/28/14. CGA will be doing the research for Oak Ridge Extension. 30% plans were submitted on November 14, 2014. Completed check and returned to CGA on 5/12/15.
- 15. Sally Bull Hollow Designer: Guy Engineering. R/W submitted the ownership research to Guy Engineering 12/17/13. 25% of preliminary design has been completed. Met with Guy Engineering on October 07, 2014 to review options on for bridge to replace low water crossing.
- 16. The following projects are pending design
 - Chance Road
 - Greasy Rehab
 - Bidding Springs Road
 - Lyon South Road

CHEROKEE COUNTY PROJECTS:

- 1. Dreadfulwater Road Designer: A. Harris. Check complete and 30% Plan in Hand conducted on 4/29/14. Revisions were made from Plan in Hand. After the Preliminary Community Meeting held on September 18, 2014 the Roads department received one comment form from a concerned landowner. Plans are approximately 75 % complete.
- 2. Hulbert-Lost City Designer: A. Harris. Coordination with utility companies are underway. Final revisions of design were submitted 4/9/15.
- 3. Lost City Road Designer: Holloway Updike & Bellen. Right of way research is complete. Plans are 60% complete.
- 4. Northeast Fort Gibson- Designer: Holloway Updike & Bellen. Sent 90% check to HUB for revisions and final plans. ABB survey was negative. R/W

COMMUNITY SERVICES COMMITTEE REPORT

started acquisition 7/8/14, out of 129 parcels 102 parcels have been acquired. 9/16/15 Four parcels were turned over to the county commissioners, two to Muskogee county and two to Cherokee county for condemnation.

- 5. Tenkiller School –Designer: Red Plains. Contractor: Glover & Associates. Contract amount \$3,747,954.02. This project was advertised to receive bids in July and bids were accepted in August. Two bids were submitted with one of the two being incomplete. Glover & Associates has been selected as the contractor for this project. A preconstruction meeting is in the process of being scheduled.
- 6. Ross Street- Designer: D. Moore Survey is complete. Preliminary design is started. Attended the Infrastructure kick off meeting to allow CN departments and the City of Tahlequah to share with the Project Team for Hastings new hospital to share their knowledge of site issues. Still waiting to know where Hasting plans for driveway entrance. Waiting for Pavement design and hydrology from CGA.
- 7. Mud Valley Road Began preliminary design criteria. Preliminary meeting was held on February 17, 2015, 6:00 PM at the Cherokee Elder Center on 4th street. Roads department have received numerous Public comment forms back. At this time they are being analyzed.
- 8. The following projects are pending design:
 - Job Corps Access Road
 - 4-Mile Road

CRAIG COUNTY PROJECTS:

- 1. NS-4340 Road Designer: Guy Engineering (Contracted through the county). Held preliminary community meeting for the project 4/15/14 at the White Oak school cafeteria. R/W videoed the project and sent a copy of the video to Guy Engineering. 7/8/2015 R/W received Trust & Restricted documents from Guy Engineering for check. Currently preparing a list of corrections needed on the documents. Received Geotechnical Report on 8/4/14. Project design 70% complete. Field meeting for utility relocation will be May 5, 2015.
- 2. NS-4410 Road (7th Street/Turnpike Bridge) Designer: Guy Engineering (Contracted through the county). Cherokee Nation has signed the agreement between Cherokee Nation, Craig County, and ODOT.

DELAWARE COUNTY PROJECTS:

- 1. D0525 Road Designer: Scott & Associates. Submitted 30% plans, hydrology, and geotechnical report. Had 30% plan in hand on April 8, 2015.
- 2. Jay/Kenwood Bridges (Bridges 53, 67, 68, and 71) Designer: Rose & McCrary, P.C. Contractor: Paradigm. Contract Amount \$5,592,242.85. Construction began June 9 2014 project74%. Meeting with HUB on 6/25/15 for pavement design.
- 3. Kansas-Bull Hollow Designer: Scott & Associates. 60% Plan in Hand was conducted on April 8, 2015. R/W finished checking all other documents. R/W

COMMUNITY SERVICES COMMITTEE REPORT

- received the utility easements and exhibits 5-20-15. 7/8/2015 R/W is currently checking the utility documents.
- 4. Kansas Dry Creek Project- Designer: Holloway Updike & Bellen. 90% plans were submitted for review on 5/10/2013. Meeting was held with HUB and Flood Plain Administrator on December 17, 2014 about Zone A issues. Still working on resolving this problem. R/W will submit for appraisals as needed.
- 5. Leach/Kenwood Road Designer: D. Moore. R/W acquisition complete. Sent floodplain permit in for approval on 1/28/15. Final review and preparing contract for bid.

MAYES COUNTY PROJECTS:

- 1. Wickliffe Bridge (Salina/Kenwood)- Designer: Guy Engineering (Contracted through the county). Contractor Bronze Oak. Contract amount \$1,774,841.63. Work began 7-9-14 project 80%
- 2. Chimney Rock Hollow I & II Designer: Guy Engineering (Contracted through the county). Received 30% plans on 3/10/14.

3.

MUSKOGEE COUNTY PROJECTS:

- 1. Northeast Fort Gibson- Designer: Holloway Updike & Bellen. Sent 90% check to HUB for revisions and final plans. ABB survey was negative. R/W started acquisition 7/8/14, out of 129 parcels. 102 parcels have been acquired. 9/16/15 Four parcels were turned over to the county commissioners, two to Muskogee county and two to Cherokee county for condemnation.
- 2. Ross Road Rehab Designer: D. Moore. Construction 100% complete and will be removed from this report next month
- 3. Texanna Road Designer: TBD. R/W is currently doing property research.

ROGERS COYNTY PROJECTS:

1. Sequoyah West I & II – Designer: TBD

SEQUOYAH COUNTY PROJECTS:

- 1. Moonshine Road Designer: J. Shehi. Preliminary survey complete. Began preliminary design. Task order received 9/18/14. Project tested positive on the ABB survey. Construction will be postponed until we get a negative test.
- 2. Dwight Mission/Sequoyah Landing Road Designer: TBD
- d) CHEROKEE TRANSIT SYSTEM: A new route that was started under the Demand Response Program will be posted as a fixed route October 1, 2015.

COMMUNITY SERVICES COMMITTEE REPORT

Ridership on all five current routes for the month of August 2015 are:

- 1. Sallisaw to Tahlequah 196 rides
- 2. Pryor to Catoosa 943 rides
- 3. Salina to Tahlequah 125 rides
- 4. Stilwell to Tahlequah 61 rides
- 5. Muskogee to Tahlequah 140 rides
- 6. Tahlequah to Claremore 119 rides
- 7. Jay to Tahlequah 160 rides
- 8. Tahlequah to Catoosa 661 rides
- 9. Stilwell to West Siloam Springs 196 rides
- 10. Tahlequah to Muskogee 135 rides
- 11. Individual Demand Response Trips: 6,257

Note: Ridership reports run 2 month behind.

Commerce Group: Commerce	Month/Year of Report:	October 2015
--------------------------	-----------------------	--------------

Executive Director: Anna Knight Phone: 453-5532 Email: aknight@cherokee.org

a. Program highlights

1. Mortgage Assistance Program Activity:

MAP Applicants	
Received MAP and purchased a home	148
Applications under review (application received, verifying applicant's eligibility)	161
Applicants capable of purchasing a home within the next 90 days	86
Applicants in short term financial coaching (applicant working on minor credit issues and/or small debt reduction; may be ready to purchase a home within 12 months)	95
Applicants in long term financial coaching (applicant working on significant credit issues and or major debt reduction; may be ready to purchase a home in 1 to 3 years)	342

The iSave Program is such a great program. It helped me set goals and achieve them; plus it felt great and was comforting to know I had money saved!

Bonita F., iSave client


- 2. The Consumer Financial Protection Bureau's Know Before You Owe mortgage initiative takes effect October 1st. These regulations were created to simplify the information provided to mortgage loan applicants in order to ensure the applicant fully understands the terms of the mortgage loan. In addition, the new regulations require the lender to give the applicant three business days to review the final closing disclosures.
- 3. Since FY07, **629 families unable to obtain a non-predatory mortgage on their own** have completed self-sufficiency counseling and obtained a non-predatory mortgage.
- 4. YTD, Self Sufficiency staff members have worked with 13 families facing foreclosure. 3 families have stopped attending the program and 1 family received a modification and saved their home, 4 families received a foreclosure prevention loan from the Small Business Assistance Center and 5 families are currently working with SBAC staff to save their home.
- 5. 1,208 consumer loans totaling \$1,336,476.20 have been made through the Small Business Assistance Center as of August 20th. 5 of these were Foreclosure Prevention loans totaling \$166,329.52.
- 6. 108 families have used Mortgage Assistance to purchase a home this fiscal year.

MAP used in conjunction with a HUD 184 loan	104
MAP used with other loan products	44
Families Housed with Mortgage Assistance	148

7. MAP household averages:

Household income	\$37,442.32
Increase in Self Sufficiency Client credit score	36 points
Debt to income including mortgage	28.1%
Debt to income ratio reduction as a result of coaching	5%
Home price	\$93,447.96

8. Mortgage Assistance usage by district:

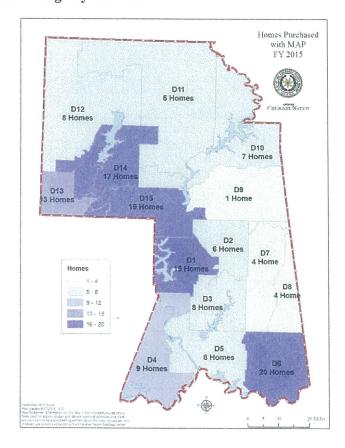

b. Annual Goals

Objective	Metric	Year to Date Achievement Notes/Comments
Homeownership Training	# of Families Attending Homeownership Training	620
Families Increasing Financial Management Skills	# of Families Increasing Skills	741
Self Sufficiency Counseling – Household Budgeting, Debt Reduction, & Credit Coaching	# of Families Actively Pursuing Goals or Achieved Goals	597 Families a. 531 families actively pursuing goals • 2% financial prosperity • 14% financial success • 18% financially stable • 64% financially instable 66 families have completed self- sufficiency counseling and obtained a non-predatory mortgage
Match Savings Program	# Active Participants	405

c. Training Schedule

Workshops and Classes				
Date	Location	Time	Workshop	
September 30	Tahlequah	TBD	Health Fair Booth	
October 5 – 6	Claremore	10 am to 5 pm	Homebuyers Training	
October 6	Cherokee County DHS	TBD	Financial Literacy Class	
October 12	Webber Falls Head Start	TBD	Financial Literacy Class	
October 13 – 14	Jay	10 am to 5 pm	Homebuyers Training	
October 14 & 21	Sequoyah High School	1 pm to 2 pm	Financial Literacy Class	
October 15	ICTC	TBD	Financial Literacy Class	
October 19 – 21	Tahlequah	4 pm to 8 pm	Homebuyers Training	
October 26	WSS Casino	TBD	Credit Counseling	
October 27 – 28	Sallisaw	10 am to 5 pm	Homebuyers Training	
October 29	Will Rogers Down	TBD	Creative Christmas Ideas	
October 30	Hard Rock Casino	8 am to 5 pm	Credit Counseling	
November 2 – 4	Claremore	4 pm to 8 pm	Homebuyers Training	
November 6	Cherokee County DHS	TBD	Financial Literacy Class	
November 10	WRD Casino	TBD	Creative Christmas Ideas	
November 12	Webber Falls Head Start	TBD	Financial Literacy Class	
November 14 & 21	Sequoyah High School	1 pm to 2 pm	Financial Literacy Class	

Commerce Group

November 16 – 17	Tahlequah	10 am to 5 pm	Homebuyers Training
November 17 – 19	Sallisaw	4 pm to 8 pm	Homebuyers Training
November 23	ICTC	TBD	Financial Literacy Class
November 24 -25	Annual ECU Conference	TBD	Annual ECU Conference
November 27	Catoosa	TBD	ICW Foster Care Budget Class
November 30	Hard Rock Casino	8 am to 5 pm	Credit Counseling
December 1 – 2	Claremore	10 am to 5 pm	Homebuyers Training
December 7 - 9	Tahlequah	4 pm to 8 pm	Homebuyers Training
December 14 – 16	Sallisaw	10 am to 5 pm	Homebuyers Training
